M. A. R. 57 (Rule 116) **No. D**

Measurement Book

Serial No. .....

58019

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency..... K.R.T.D.I. .....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Name of work :- Development work in W-13 Mallasandra. Est cost :- 50.00 Lakhs Job. Code :- 013-17-000082 Pcode P-0[illegible]2HLS A.A. NO. :- JC/D/AS/PR/23/16-17, Date :- 05.06.2017 T.S. NO :- CE/D7/TS/60/16-17, Date :- 12.06.2017. Agr NO :- EE/DD/AGR/113/2017-18.						

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
8.	Cement Concrete pavement Construction of un-reinforced Plain Cement Concrete pavement thickness as per design, over a Prepared Sub base with OPC Cement or any other type as per Clause 1051.2.2. With 25mm and down Size graded granite metal Coarse aggregate and fine aggregate with Superplastisier ~~if~~ is Complete as per Specification.						
	5th cross Ravindra Nagara	1X3	30.00	$\frac{6.5+7.5+7.0}{3}$	$\frac{0.155+0.145}{2}$	94.50	
		1X1	20.00	$\frac{7.1+6.5+7.5}{3}$	$\frac{0.145+0.155}{2}$	21.00	
	4th cross Ravindranagara	1X2	30.00	$\frac{5.5+4.5}{2}$	$\frac{0.16+0.14}{2}$	45.00	
		1X1	10.00	$\frac{4.5+5.5}{2}$	$\frac{0.14+0.16}{2}$	7.50	
						168.00	m^3

EXECUTIVE ENGINEER
Bruhat Bangalore Mahanagara[illegible]e
Basarahalli Division, Bangalore-57

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

Serial No. 58023

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
		@Rs 6217.96/m³					10,44,617=00
9.	Providing T.M.T Steel reinforcement for R.C.C. work including straightening, cutting bending, hooking, placing in position, lapping and/or welding required tying with binding wire and anchoring to the adjoining members wherever necessary all completed as per specification						
	Qty B/F from P/N 58060 of this MB	P.N 58060				9.07	tonnes
		@Rs 74331.44/tonne					6,74,334=00
							674186=00

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

Serial No. 58024

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions			Contents	Reference to last Measurement
		Number	Length	Breadth / Depth		
1	2	3	4	5 / 6	7	8
					126.00	m^2
		@Rs 1680=00/m^2				2,11,680=00
						45760=00
	Certificate				Total	₹ 4,57,6,603=00
	Certifies that the work is done Satisfactorily				Add KRIDL Charges(9%)	= 4,11,894.27
						411850=00
				28/12/17	Grand total	49,88,497.27
						4988340=00

ಸಹಾಯಕ ಕಾರ್ಯನಿರ್ವಾಹಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬಿಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Audited and admitted for Rs. 498340=00

Passed by Cheque for Rs. 450958=00

( )

by adjus. 47382=00

Accounts Superintendent

Exe. Engineer

S.P.M.P. Dasarahalli Division

Scanned by CamScanner

M. A. R. 57 (Rule 116) **No. D**

Measurement Book

53025

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions			Contents	Reference to last Measurement
		Number	Length	Breadth / Depth		
1	2	3	4	5 / 6	7	8

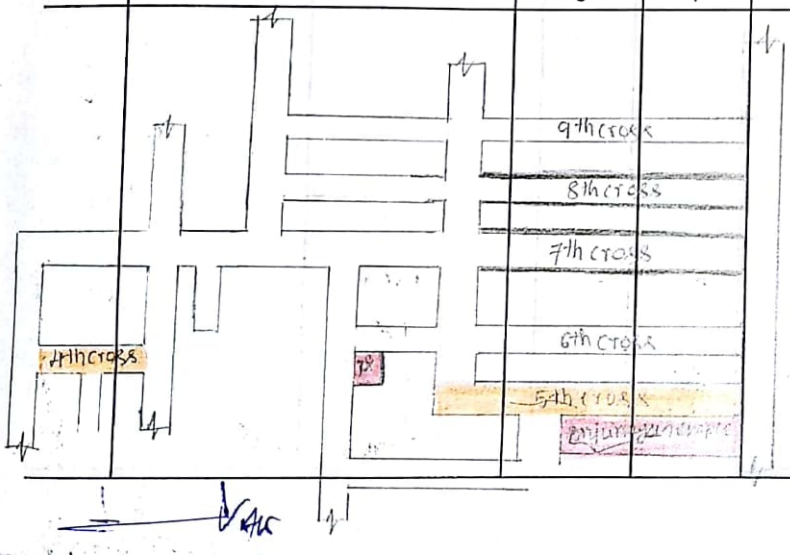

INDEX

- RCC Drain
- C.C. Road
- Temples

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಶೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ

Scanned by CamScanner
